




# Detail Gradation Statistical Summary Report

**Plant** 1050-Independent North Mine (FDOT Pit #11-490)  
**Product** 1009-Concrete Sand  
**Specification**  
**Period** 03/19/2020 - 03/26/2020

Sieve/Test	Tests	Average	Min	Max	Range	St Dev	Target	Specification	PWS
#4 (4.75mm)	6	0.0	0.0	0.0	0.0	0.00			
#8 (2.36mm)	6	0.1	0.0	0.2	0.2	0.08			
#16 (1.18mm)	6	4.7	2.6	7.6	5.0	2.01			
#30 (0.6mm)	6	25.0	21.4	31.4	10.0	4.12			
#50 (0.3mm)	6	68.9	62.3	74.7	12.4	4.24			
#100 (0.15mm)	6	96.9	92.4	99.0	6.6	2.50			
#200 (75µm)	6	99.9	99.8	99.9	0.1	0.05			
Pan	6	100.0	100.0	100.0	0.0	0.00			
Total Moisture	6	4.1	3.3	5.6	2.3	0.84			
FM	6	1.96	1.88	2.02	0.14	0.055			

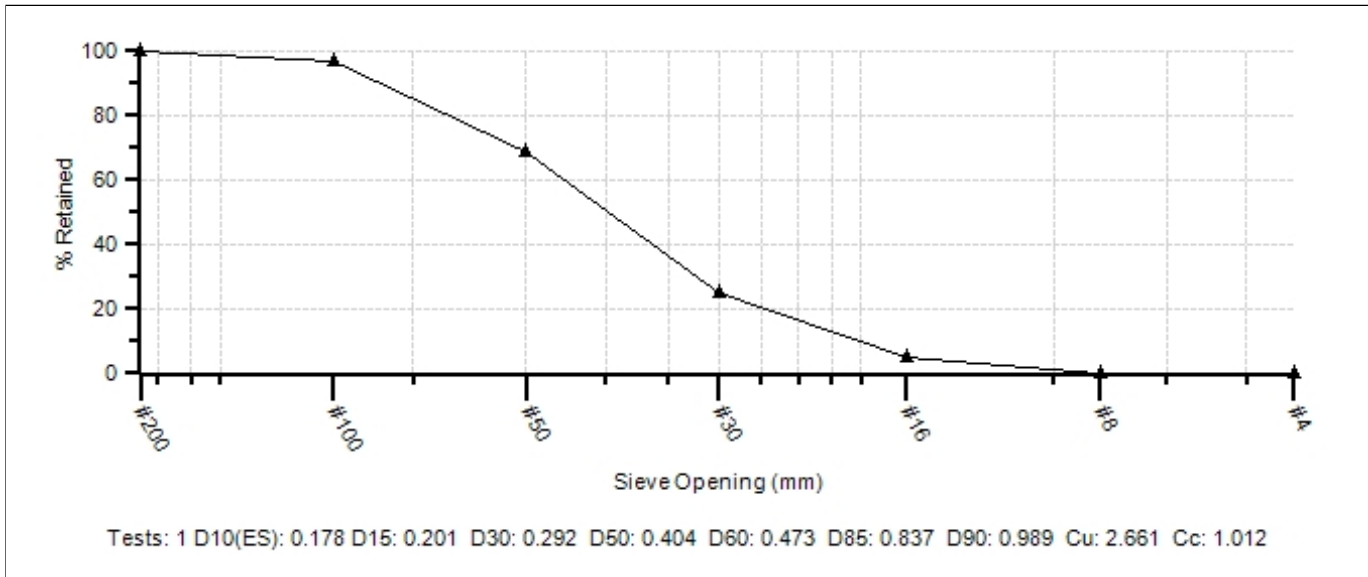

**Comments**

**Query** Query Selections  
 Date Created 03/26/2020  
 Date Range 03/19/2020 - 03/26/2020  
 Plant Independent North Mine (FDOT Pit #11-490)-1050  
 Sample Type Shipping
