




Basic Quality Statistical Summary Report

Plant 1050-Independent North Mine (FDOT Pit #11-490)
Product 1009-Concrete Sand
Specification Concrete Sand
Period 12/23/2021 - 12/30/2021

Sieve/Test	Tests	Average	St Dev	Target	Specification
#4 (4.75mm)	5	100.0	0.00		95-100
#8 (2.36mm)	5	98.7	0.43		85-100
#16 (1.18mm)	5	90.3	1.73	67-98	65-99
#30 (0.6mm)	5	66.3	3.53	27-79	25-80
#50 (0.3mm)	5	31.6	2.17	7-38	5-40
#100 (0.15mm)	5	1.9	0.26	0-6	0-7
#200 (75µm)	5	0.1	0.05		0-4
Pan	5	0.0	0.00		
<hr/>					
Total Moisture	4	4.4	0.82		
FM	5	2.11	0.075	1.87-2.18\2	1.85-2.2

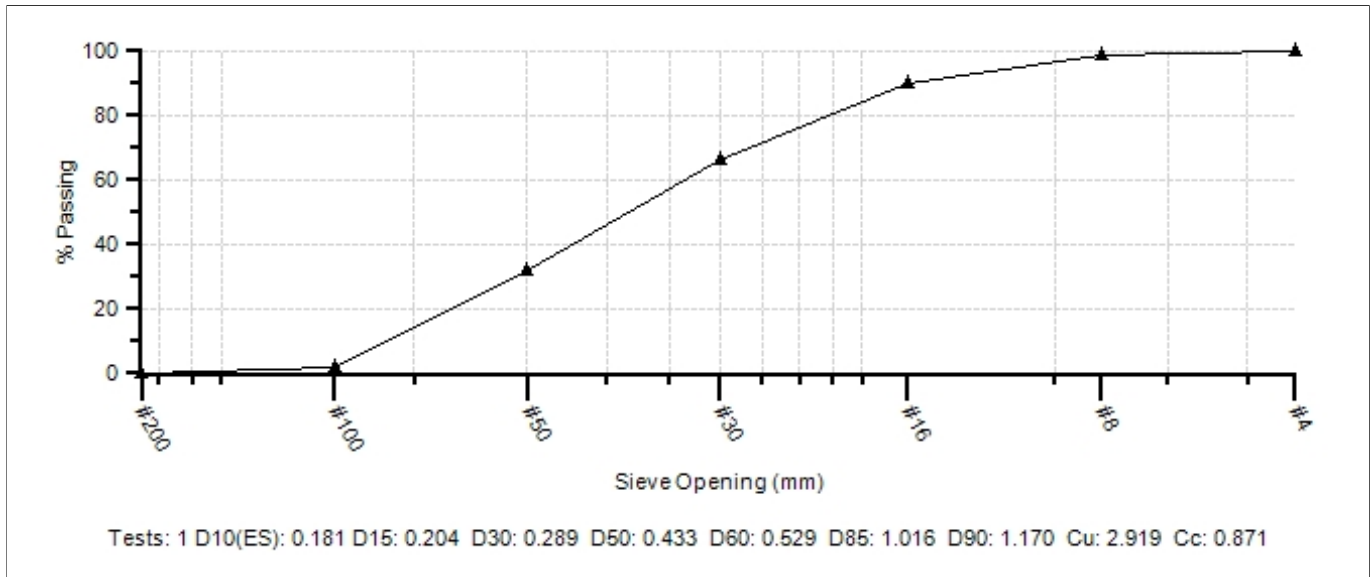

Query Query Selections
 Date Created 12/30/2021
 Date Range 12/23/2021 - 12/30/2021
 Plant Independent North Mine (FDOT Pit #11-490)
 Sample Type Shipping
