




Basic Quality Statistical Summary Report

Plant 1050-Independent North Mine (FDOT Pit #11-490)
Product 1009-Concrete Sand
Specification Concrete Sand
Period 10/18/2022 - 10/25/2022

Sieve/Test	Tests	Average	St Dev	Target	Specification
#4 (4.75mm)	5	100.0	0.00		95-100
#8 (2.36mm)	5	98.8	0.42		85-100
#16 (1.18mm)	5	89.1	1.83	67-98	65-99
#30 (.6mm)	5	62.8	4.46	27-79	25-80
#50 (.3mm)	5	35.6	6.19	7-38	5-40
#100 (.15mm)	5	3.4	0.98	0-6	0-7
#200 (75µm)	5	0.1	0.05		0-4
Pan	5	0.0	0.00		
FM	5	2.10	0.133	1.87-2.18\2	1.85-2.2
Total Moisture	5	4.5	1.44		

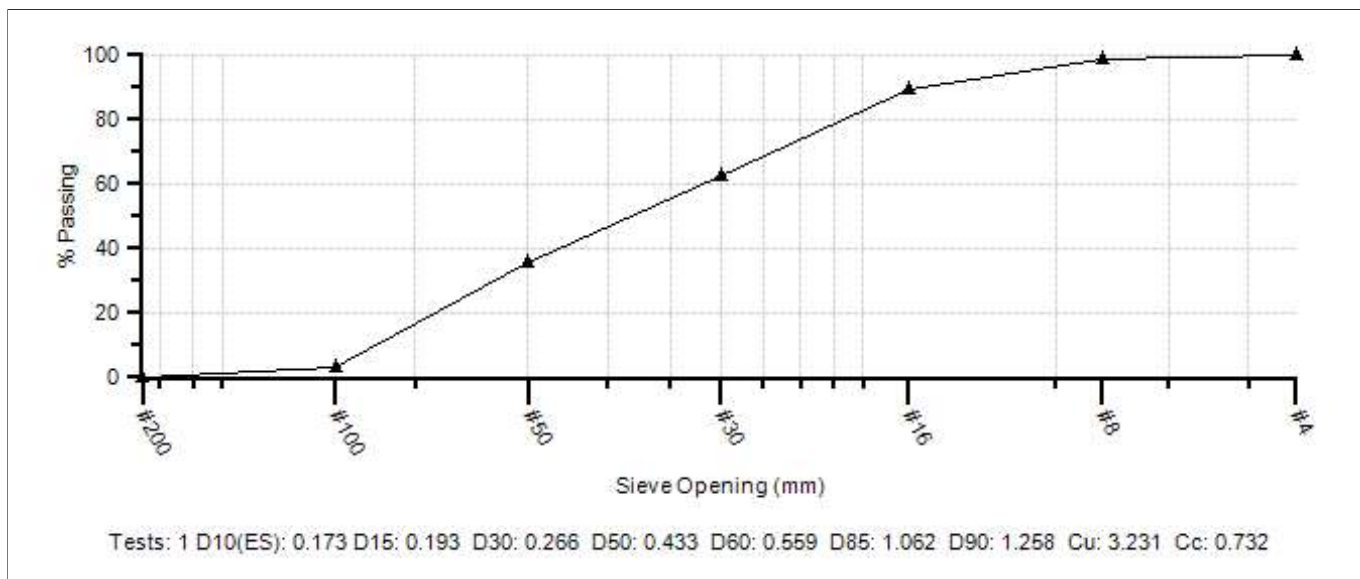

Query

Query Selections
Date Created 10/25/2022
Date Range 10/18/2022 - 10/25/2022
Plant Independent North Mine (FDOT Pit #11-490)
Sample Type Shipping
