




Basic Quality Statistical Summary Report

Plant 1050-Independent North Mine (FDOT Pit #11-490)
Product 1009-Concrete Sand
Specification Concrete Sand
Period 12/27/2022 - 01/03/2023

Sieve/Test	Tests	Average	St Dev	Target	Specification
#4 (4.75mm)	4	100.0	0.00		95-100
#8 (2.36mm)	4	99.7	0.00		85-100
#16 (1.18mm)	4	93.2	0.68	67-98	65-99
#30 (.6mm)	4	67.0	2.85	27-79	25-80
#50 (.3mm)	4	26.8	2.44	7-38	5-40
#100 (.15mm)	4	2.5	0.43	0-6	0-7
#200 (75µm)	4	1.2	0.99		0-4
Pan	4	0.0	0.00		
FM	4	2.11	0.059	1.87-2.18\2	1.85-2.2
Total Moisture	4	4.2	0.57		

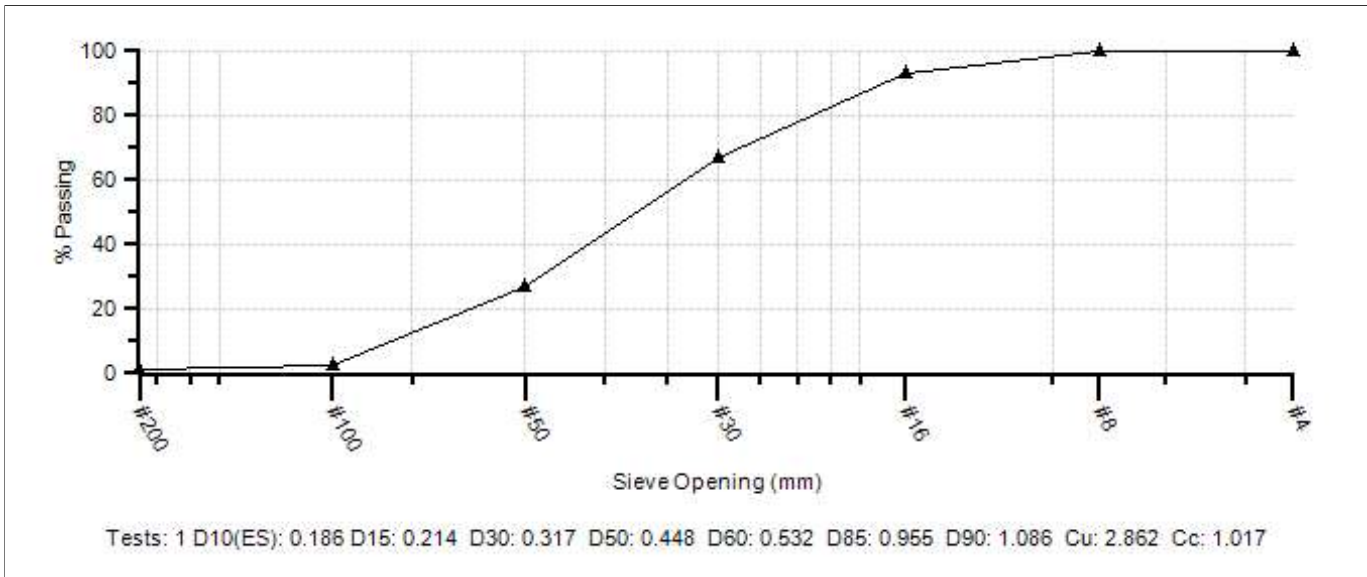

Query

Query Selections
Date Created 01/03/2023
Date Range 12/27/2022 - 01/03/2023
Plant Independent North Mine (FDOT Pit #11-490)
Sample Type Shipping
