




Basic Quality Statistical Summary Report

Plant 1050-Independent North Mine (FDOT Pit #11-490)
Product 1009-Concrete Sand
Specification Concrete Sand
Period 01/26/2024 - 02/02/2024

Sieve/Test	Tests	Average	St Dev	Target	Specification
#4 (4.75mm)	5	100.0	0.04		95-100
#8 (2.36mm)	5	99.7	0.15		85-100
#16 (1.18mm)	5	95.2	1.18	67-98	65-99
#30 (.6mm)	5	71.1	4.13	27-79	25-80
#50 (.3mm)	5	26.8	4.58	7-38	5-40
#100 (.15mm)	5	2.2	0.92	0-6	0-7
#200 (75µm)	5	0.1	0.00		0-4
Pan	5	0.0	0.00		
FM	5	2.05	0.106	1.87-2.18\2	1.85-2.2
Total Moisture	5	3.4	0.29		

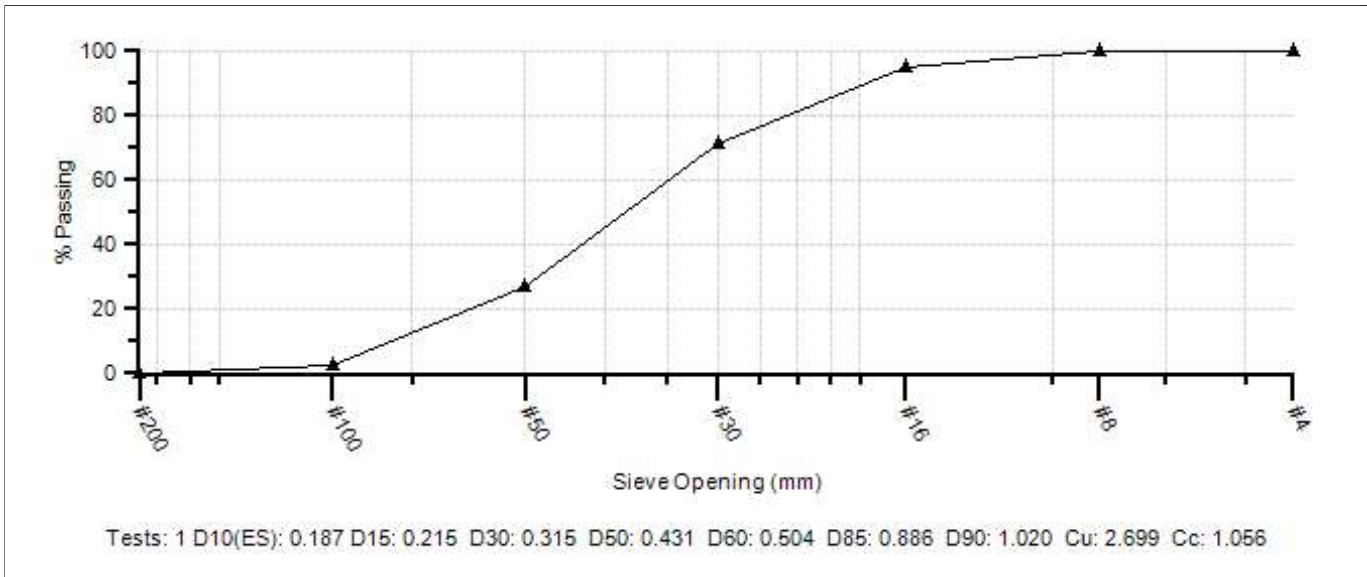

Query

Query Selections
Date Created 02/02/2024
Date Range 01/26/2024 - 02/02/2024
Plant Independent North Mine (FDOT Pit #11-490)
Sample Type Shipping
