




Basic Quality Statistical Summary Report

Plant 1030-Haines City Mine (FDOT Pit #16-024)
Product 1009-Concrete Sand
Specification Concrete Sand
Period 07/19/2024 - 07/26/2024

Sieve/Test	Tests	Average	St Dev	Target	Specification
#4 (4.75mm)	7	100.0	0.00	95-100	95-100
#8 (2.36mm)	7	99.9	0.05	85-100	85-100
#16 (1.18mm)	7	95.7	0.77	65-98	65-100
#30 (.6mm)	7	69.1	2.52	25-75	≥25
#50 (.3mm)	7	36.6	3.83	5-44	5-45
#100 (.15mm)	7	7.3	2.51	0-10	0-10
#200 (75µm)	7	0.1	0.08	0-4	0-4
Pan	7	0.0	0.00		
FM	7	1.92	0.083	1.8-2.2\2	
Total Moisture	7	3.3	0.30	0-5	0-6
D10 (ES)	7	0.16	0.010		
D50	7	0.40	0.027		
D60	7	0.49	0.028		
Cc	7	0.85	0.059		
Cu	7	3.09	0.171		

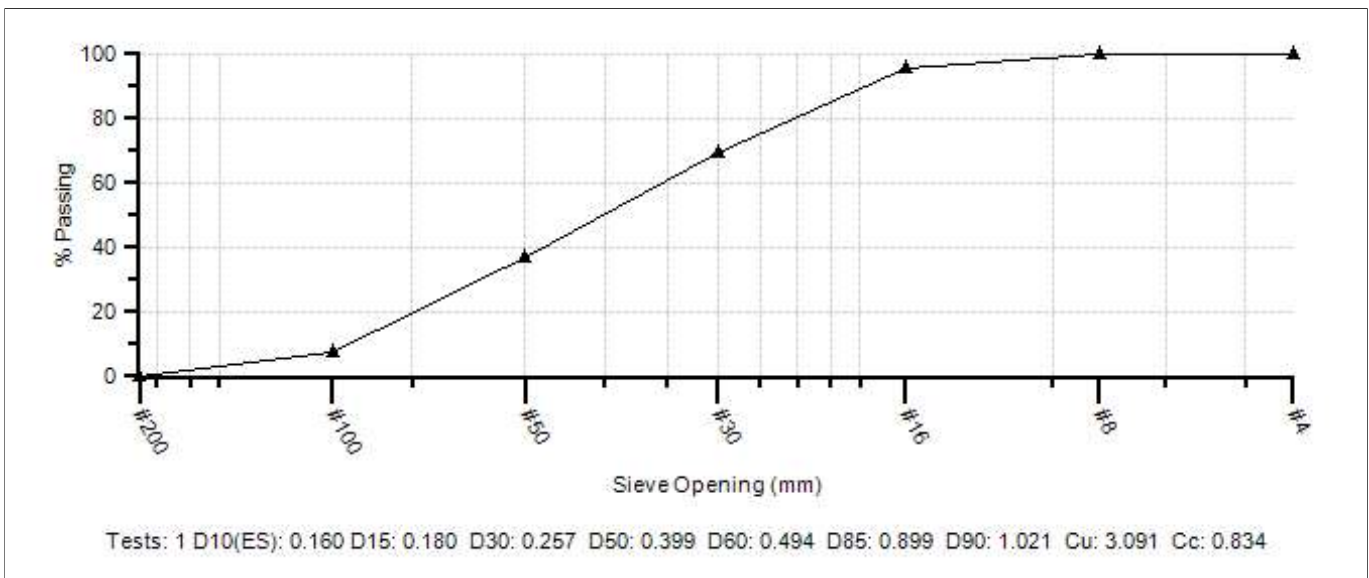

Query

Query Selections

Date Created 07/26/2024

Date Range 07/19/2024 - 07/26/2024

Plant Haines City Mine (FDOT Pit #16-024)

Sample Type Shipping
