




Basic Quality Statistical Summary Report

Plant 1070-Independent South Mine (FDOT Pit#11-298)
Product 1009-Concrete Sand
Specification Concrete Sand
Period 07/19/2024 - 07/26/2024

Sieve/Test	Tests	Average	St Dev	Target	Specification
#4 (4.75mm)	5	99.9	0.09		95-100
#8 (2.36mm)	5	98.8	0.11		85-100
#16 (1.18mm)	5	91.6	1.09	67-98	65-99
#30 (.6mm)	5	71.3	3.46	27-79	25-80
#50 (.3mm)	5	45.5	3.59	7-38	5-40
#100 (.15mm)	5	7.3	0.94	0-6	0-7
#200 (75µm)	5	0.2	0.09		0-4
Pan	5	0.0	0.00		
FM	5	1.855	0.0771	1.87-2.18\2	1.85-2.2
Total Moisture	5	5.961	1.7086		
D10 (ES)	5	0.16	0.004		
D50	5	0.34	0.033		
D60	5	0.44	0.038		
Cc	5	0.74	0.025		
Cu	5	2.81	0.230		

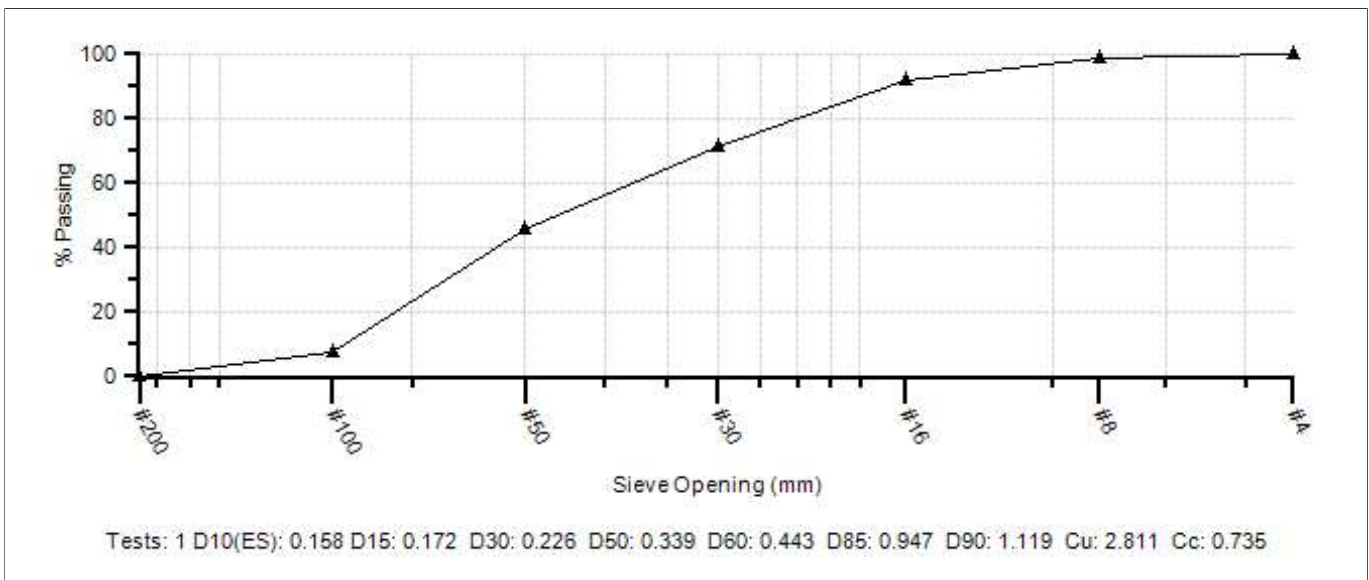

Query

Query Selections
Date Created 07/26/2024
Date Range 07/19/2024 - 07/26/2024
Plant Independent South Mine (FDOT Pit#11-298)
Sample Type Shipping
