




Basic Quality Statistical Summary Report

Plant 1050-Independent North Mine (FDOT Pit #11-490)
Product 1009-Concrete Sand
Specification Concrete Sand
Period 08/27/2024 - 09/03/2024

Sieve/Test	Tests	Average	St Dev	Target	Specification
#4 (4.75mm)	5	100.0	0.00		95-100
#8 (2.36mm)	5	99.8	0.13		85-100
#16 (1.18mm)	5	96.2	1.50	67-98	65-99
#30 (.6mm)	5	77.1	5.71	27-79	25-80
#50 (.3mm)	5	29.9	3.65	7-38	5-40
#100 (.15mm)	5	2.1	0.47	0-6	0-7
#200 (75µm)	5	0.1	0.04		0-4
Pan	5	0.0	0.00		
FM	5	1.95	0.107	1.87-2.18\2	1.85-2.2
Total Moisture	5	3.9	1.08		
D10 (ES)	5	0.1835	0.00605		
D50	5	0.40	0.028		
D60	5	0.47	0.037		
Cc	5	1.03	0.050		
Cu	5	2.56	0.125		

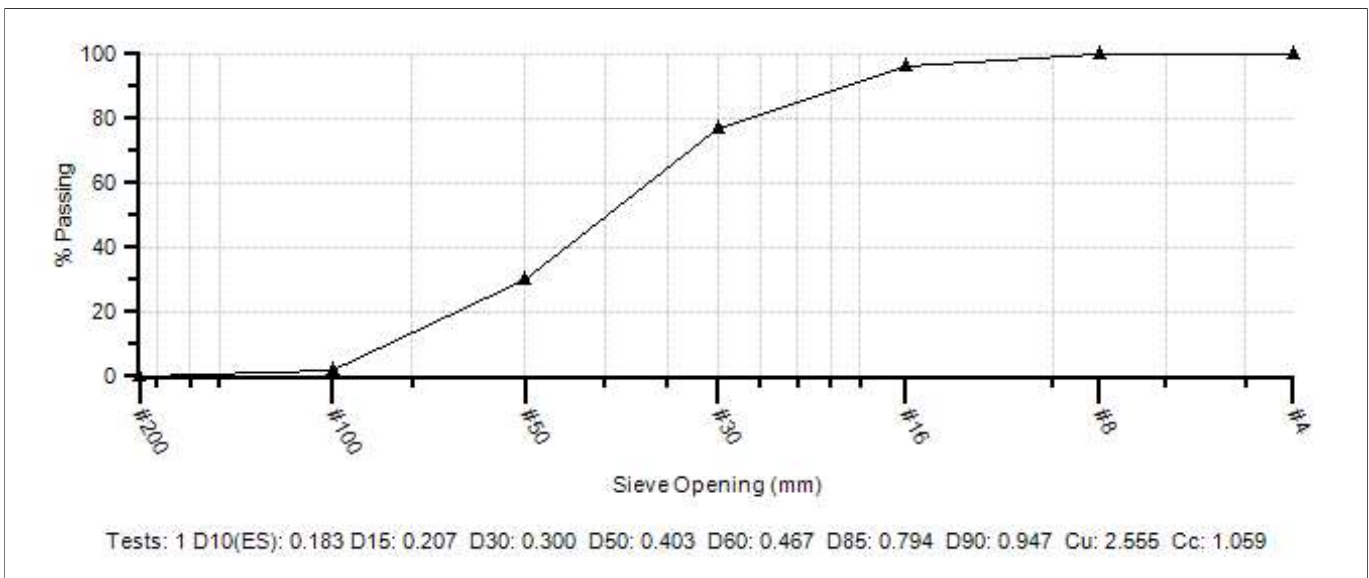

Query

Query Selections
Date Created 09/03/2024
Date Range 08/27/2024 - 09/03/2024
Plant Independent North Mine (FDOT Pit #11-490)
Sample Type Shipping
