




Basic Quality Statistical Summary Report

Plant 1070-Independent South Mine (FDOT Pit#11-298)
Product 1009-Concrete Sand
Specification Concrete Sand
Period 09/30/2024 - 10/31/2024

Sieve/Test	Tests	Average	St Dev	Target	Specification
#4 (4.75mm)	12	100.0	0.07		95-100
#8 (2.36mm)	12	98.9	0.30		85-100
#16 (1.18mm)	12	90.6	1.93	67-98	65-99
#30 (.6mm)	12	63.0	6.28	27-79	25-80
#50 (.3mm)	12	35.9	8.65	7-38	5-40
#100 (.15mm)	12	6.6	2.41	0-6	0-7
#200 (75µm)	12	0.2	0.12		0-4
Pan	12	0.0	0.00		
FM	12	2.050	0.1864	1.87-2.18\2	1.85-2.2
Total Moisture	12	4.500	0.9469		
D10 (ES)	12	0.17	0.013		
D50	12	0.43	0.080		
D60	12	0.55	0.086		
Cc	12	0.80	0.109		
Cu	12	3.33	0.317		

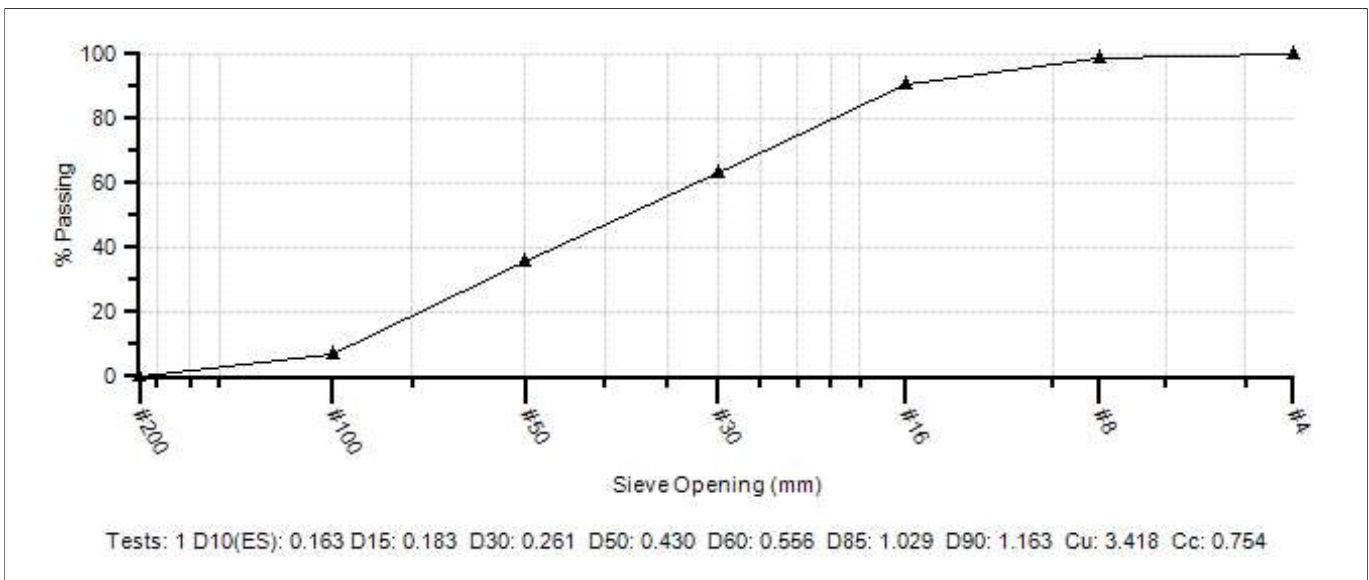

Query

Query Selections
Date Created 10/31/2024
Date Range 09/30/2024 - 10/31/2024
Plant Independent South Mine (FDOT Pit#11-298)
Sample Type Shipping
