




Basic Quality Statistical Summary Report

Plant 1050-Independent North Mine (FDOT Pit #11-490)
Product 1009-Concrete Sand
Specification Concrete Sand
Period 04/18/2025 - 04/25/2025

Sieve/Test	Tests	Average	St Dev	Target	Specification
#4 (4.75mm)	11	100.0	0.03		95-100
#8 (2.36mm)	11	99.6	0.16		85-100
#16 (1.18mm)	11	95.1	0.61	67-98	65-99
#30 (.6mm)	11	73.3	2.42	27-79	25-80
#50 (.3mm)	11	27.2	2.54	7-38	5-40
#100 (.15mm)	11	1.0	0.29	0-6	0-7
#200 (75µm)	11	0.1	0.05		0-4
Pan	11	0.0	0.00		
FM	11	2.04	0.050	1.87-2.18\2	1.85-2.2
Total Moisture	11	3.1	0.45		
D10 (ES)	11	0.1909	0.00519		
D50	11	0.42	0.014		
D60	11	0.49	0.015		
Cc	11	1.04	0.027		
Cu	11	2.58	0.060		

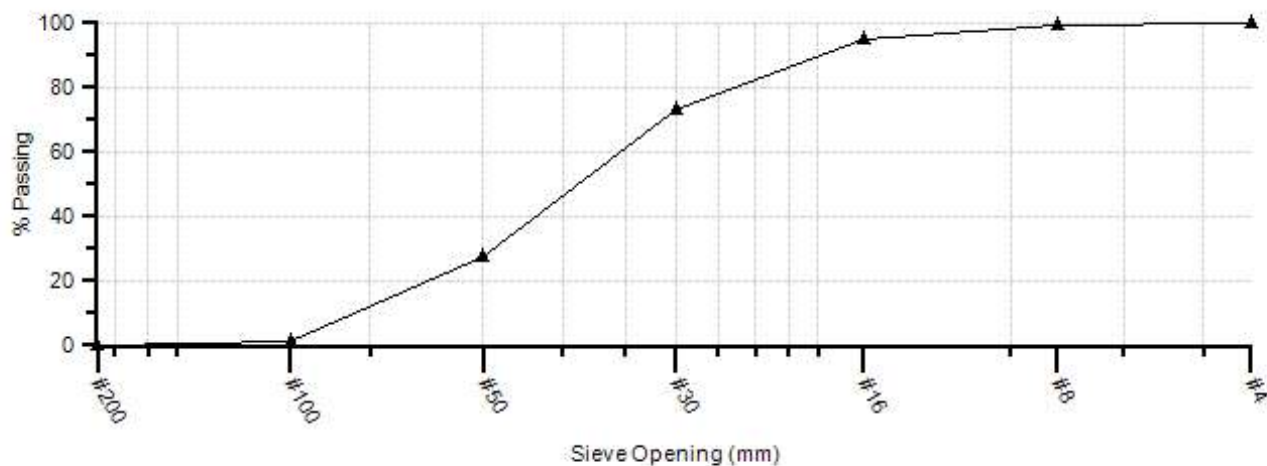

Tests: 1 D10(ES): 0.190 D15: 0.217 D30: 0.313 D50: 0.423 D60: 0.491 D85: 0.863 D90: 1.007 Cu: 2.581 Cc: 1.047

Query

Query Selections

Date Created 04/25/2025

Date Range 04/18/2025 - 04/25/2025

Plant Independent North Mine (FDOT Pit #11-490)

Sample Type Shipping
