




Basic Quality Statistical Summary Report

Plant 1050-Independent North Mine (FDOT Pit #11-490)
Product 1009-Concrete Sand
Specification Concrete Sand
Period 05/01/2025 - 05/08/2025

Sieve/Test	Tests	Average	St Dev	Target	Specification
#4 (4.75mm)	9	100.0	0.00		95-100
#8 (2.36mm)	9	99.6	0.17		85-100
#16 (1.18mm)	9	94.9	1.48	67-98	65-99
#30 (.6mm)	9	71.5	5.26	27-79	25-80
#50 (.3mm)	9	23.2	1.67	7-38	5-40
#100 (.15mm)	9	0.7	0.11	0-6	0-7
#200 (75µm)	9	0.1	0.07		0-4
Pan	9	0.0	0.00		
FM	9	2.10	0.082	1.87-2.18\2	1.85-2.2
Total Moisture	9	3.8	0.96		
D10 (ES)	9	0.2003	0.00484		
D50	9	0.44	0.022		
D60	9	0.51	0.032		
Cc	9	1.08	0.027		
Cu	9	2.55	0.109		

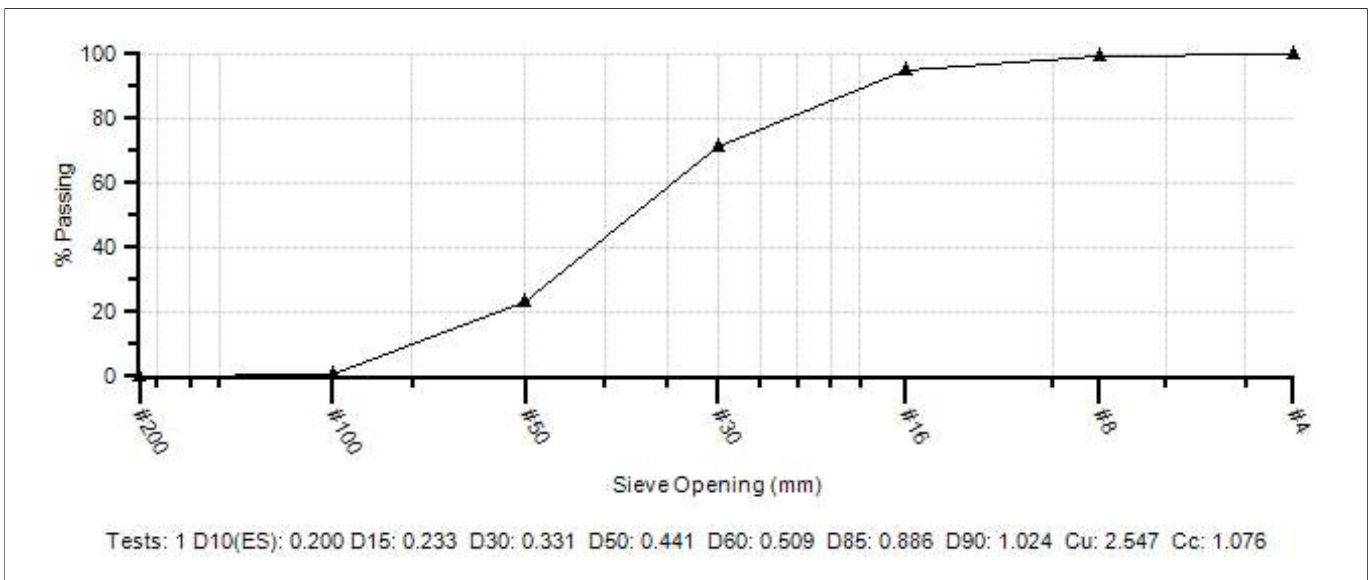

Query

Query Selections
Date Created 05/08/2025
Date Range 05/01/2025 - 05/08/2025
Plant Independent North Mine (FDOT Pit #11-490)
Sample Type Shipping
