




Basic Quality Statistical Summary Report

Plant 1030-Haines City Mine (FDOT Pit #16-024)
Product 1009-Concrete Sand
Specification Concrete Sand
Period 05/23/2025 - 05/30/2025

Sieve/Test	Tests	Average	St Dev	Target	Specification
#4 (4.75mm)	6	100.0	0.00	95-100	95-100
#8 (2.36mm)	6	99.8	0.10	85-100	85-100
#16 (1.18mm)	6	95.6	0.84	65-98	65-100
#30 (.6mm)	6	72.8	4.29	25-75	≥25
#50 (.3mm)	6	43.8	5.31	5-44	5-45
#100 (.15mm)	6	9.8	1.90	0-10	0-10
#200 (75µm)	6	0.1	0.04	0-4	0-4
Pan	6	0.0	0.00		
FM	6	1.78	0.113	1.8-2.2\2	
Total Moisture	6	5.8	3.09	0-5	0-6
D10 (ES)	6	0.15	0.010		
D50	6	0.35	0.043		
D60	6	0.44	0.050		
Cc	6	0.80	0.019		
Cu	6	3.01	0.271		

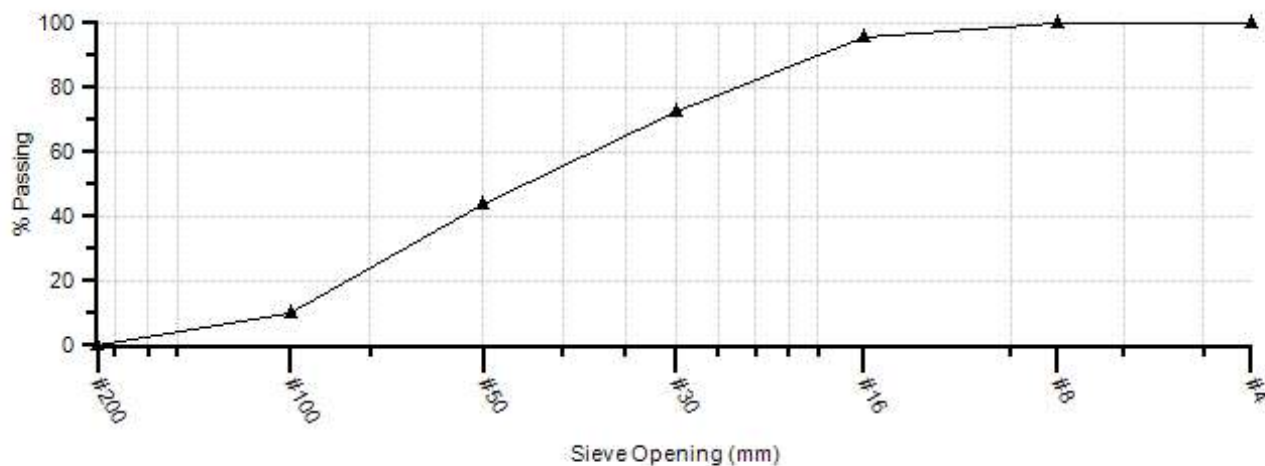

Query

Query Selections

Date Created 05/30/2025

Date Range 05/23/2025 - 05/30/2025

Plant Haines City Mine (FDOT Pit #16-024)

Sample Type Shipping
