




Basic Quality Statistical Summary Report

Plant 1050-Independent North Mine (FDOT Pit #11-490)
Product 1009-Concrete Sand
Specification Concrete Sand
Period 09/11/2026 - 09/18/2026

Sieve/Test	Tests	Average	St Dev	Target	Specification
#4 (4.75mm)	5	100.0	0.00		95-100
#8 (2.36mm)	5	99.8	0.16		85-100
#16 (1.18mm)	5	96.6	1.89	67-98	65-99
#30 (.6mm)	5	77.7	3.68	27-79	25-80
#50 (.3mm)	5	36.3	2.58	7-38	5-40
#100 (.15mm)	5	4.2	0.93	0-6	0-7
#200 (75µm)	5	0.1	0.11		0-4
Pan	5	0.0	0.00		
FM	5	1.855	0.0815	1.87-2.18\2	1.85-2.2
Total Moisture	5	3.989	0.5714		

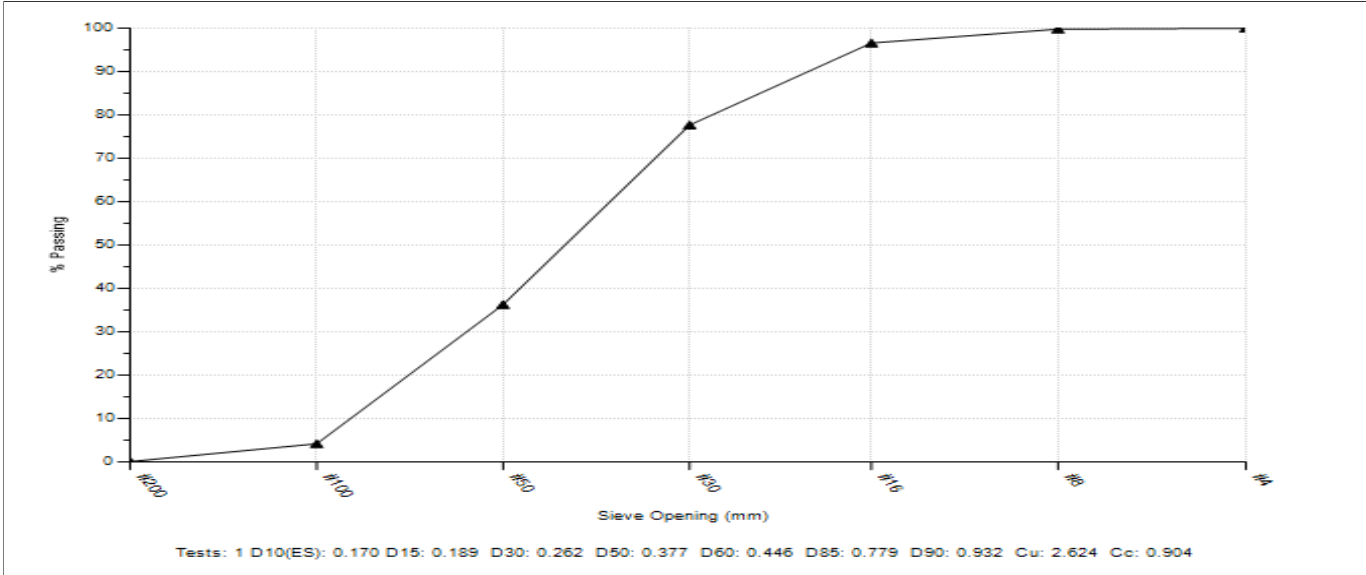

Query

Query Selections

Date Created 09/18/2026

Date Range 09/11/2026 - 09/18/2026

Plant Independent North Mine (FDOT Pit #11-490)

Product
